

Project Planning Phase

Date	03 October 2026
Team ID	SWTID-2026-1711
Project Name	Auto Ticket Classification using Flow Designer in ServiceNow
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	ServiceNow Setup	USN-1	As a developer, I can configure the ServiceNow Developer Instance for the project.	2	High	Team
Sprint-1	ServiceNow Setup	USN-2	As a developer, I can understand and configure the Incident/Service Ticket table and required fields.	2	High	Team
Sprint-1	Ticket Configuration	USN-3	As an IT user, I can create a service ticket with required details such as short description, category, and assignment group.	3	High	Team
Sprint-1	Ticket Configuration	USN-4	As a developer, I can define ticket categories and support groups for automatic classification.	3	High	Team
Sprint-1	Flow Designer	USN-5	As a developer, I can create a Flow Designer flow that is triggered when a new ticket is created.	3	High	Team
Sprint-1	Flow Designer	USN-6	As a developer, I can configure conditions in Flow Designer to identify the appropriate ticket category.	5	High	Team
Sprint-1 Total				18		
Sprint-2	Auto Classification	USN-7	As a developer, I can automatically classify tickets based on the information provided in the ticket.	5	High	Team
Sprint-2	Auto Assignment	USN-8	As a developer, I can automatically assign classified tickets to the appropriate support group.	5	High	Team
Sprint-2	Flow Actions	USN-9	As a developer, I can configure Flow Designer actions to update ticket fields automatically.	3	High	Team

Sprint-2	Testing	USN-10	As a tester, I can test the flow using different types of service tickets.	3	High	Team
Sprint-2	Error Handling	USN-11	As a developer, I can handle tickets that do not match the defined classification conditions.	2	Medium	Team
Sprint-2	Documentation	USN-12	As a project team, we can document the implementation, testing, and results of the project.	3	Medium	Team
Sprint-2 Total				21		

Total Story Points

Sprint 1 = 18 Story Points

Sprint 2 = 21 Story Points

Total = 18 + 21 = 39 Story Points

Project Tracker, Velocity & Burndown Chart: (4 Marks)

Since the project is planned for 2 sprints, the following tracker is used.

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	18	6 Days	[Start Date]	[End Date]	18	[Actual Date]
Sprint-2	21	6 Days	[Start Date]	[End Date]	21	[Actual Date]
Total	39	12 Days			39	

Note: Replace [Start Date], [End Date], and [Actual Date] with your team's actual project dates. Don't use the 2022 dates from the sample template unless your project was actually conducted then.

Velocity:

Velocity represents the amount of work, measured in Story Points, that the team completes during a sprint.

Sprint Velocity

Sprint 1 Velocity = 18 Story Points

Sprint 2 Velocity = 21 Story Points

Average Team Velocity

Average Velocity = Total Story Points Completed / Number of Sprints

$$\text{Average Velocity} = (18 + 21) / 2 = 39 / 2$$

Average Velocity = 19.5 Story Points per Sprint

Therefore, the team's average velocity for the project is 19.5 Story Points per Sprint.

Average Velocity per Day

Since each sprint is planned for 6 days:

Average Velocity per Day = Total Story Points / Total Sprint Days

$$= 39 / 12 = 3.25$$

Average Velocity = 3.25 Story Points per Day


This means the team completes approximately 3.25 Story Points per working day based on the planned two-sprint schedule.

Burndown Chart:

Burndown Chart Data

Day	Planned Remaining Story Points
Day 0	39
Day 1	35.75
Day 2	32.50
Day 3	29.25
Day 4	26.00
Day 5	22.75
Day 6	19.50
Day 7	16.25
Day 8	13.00
Day 9	9.75
Day 10	6.50
Day 11	3.25
Day 12	0

Burndown Chart

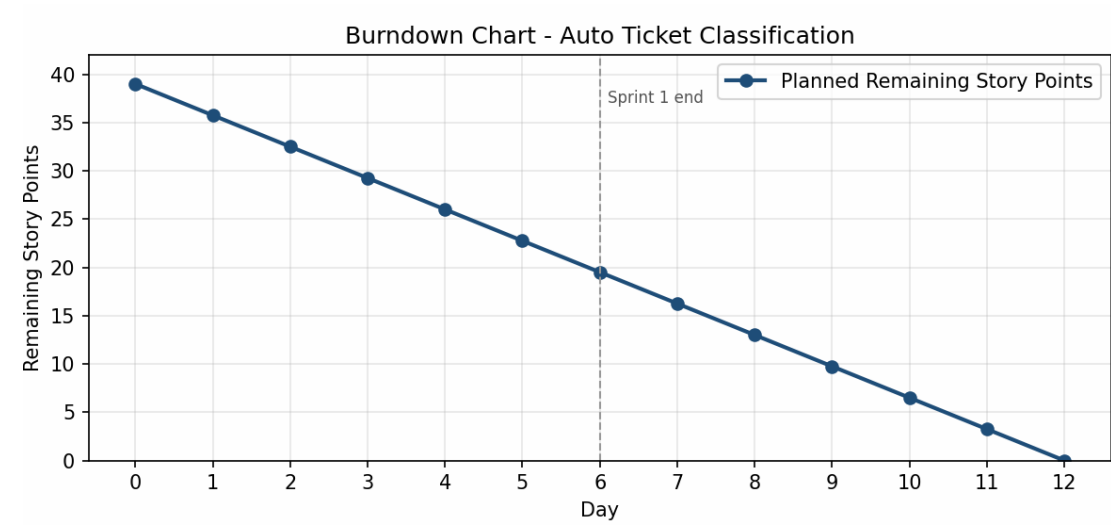

Burndown Chart Description

The Burndown Chart represents the remaining Story Points throughout the project. At the beginning of the project, there are 39 Story Points. As the team completes the user stories, the remaining work decreases. By the end of Sprint 2, all 39 Story Points are planned to be completed.

Project Flow:

ServiceNow Setup → Ticket Configuration → Flow Designer → Auto Classification → Auto Assignment → Testing → Documentation
